

# Natural environment strategies

March 2023

Parks mitigation programme

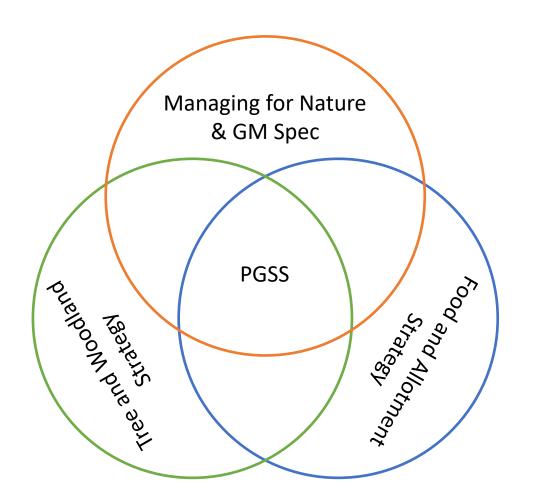




#### Workstream timelines


Project work

Mapping


Engagement

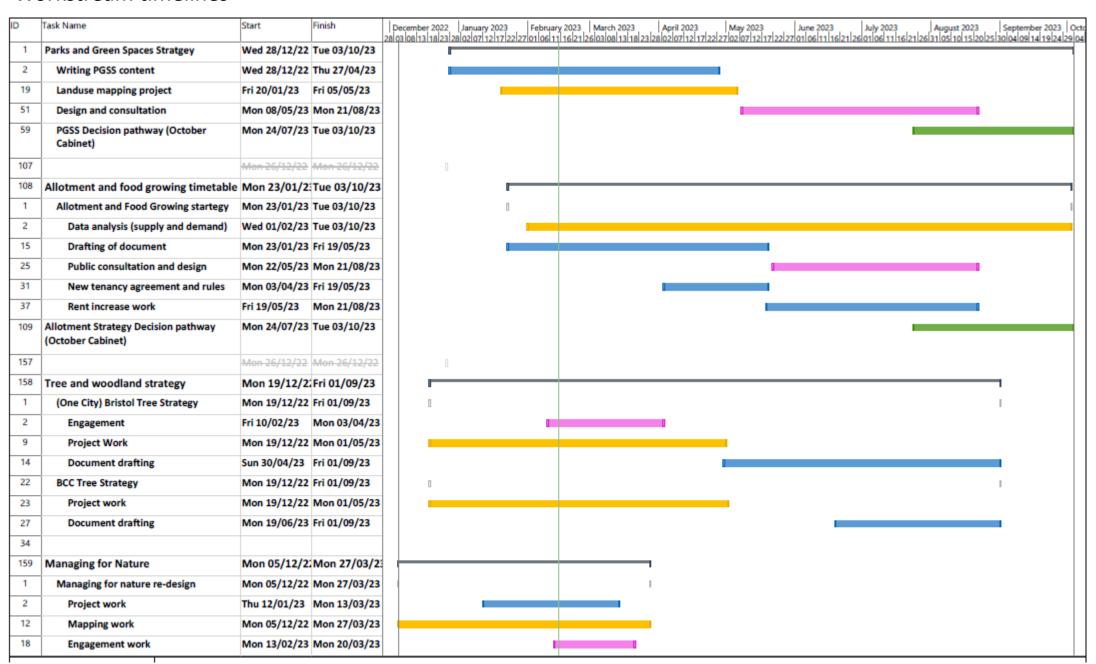

Land footprint for PGSS

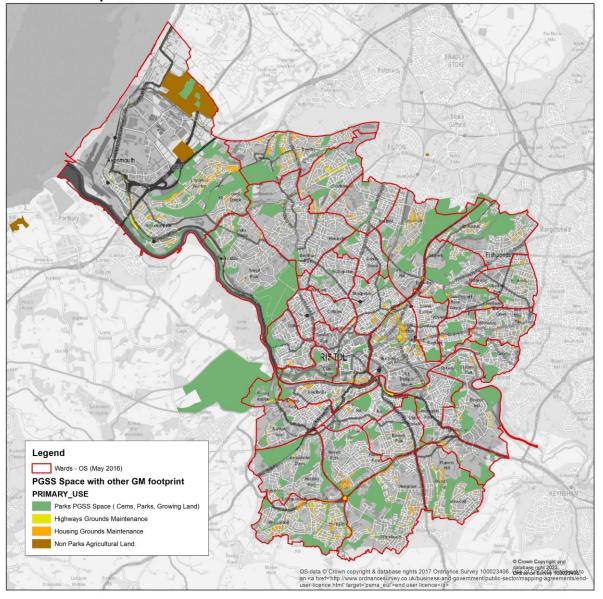

PGSS land typologies

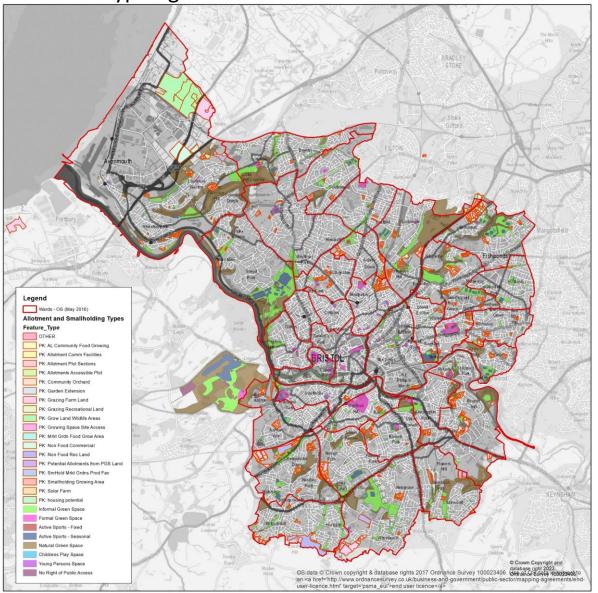

Allotments & Food Growing Strategy


Project work

Mapping

Engagement



Land covered	BCC and association allotments, Parks owned small holdings, Other potential parks land
Time span	15 years
Outputs	How to reduce allotment waiting lists, Opportunities for other land for food growing, Tenancy agreements, Fee uplift
Engagement	Public consultation June - July 23 (6 weeks)
Approval	Cabinet Oct 23

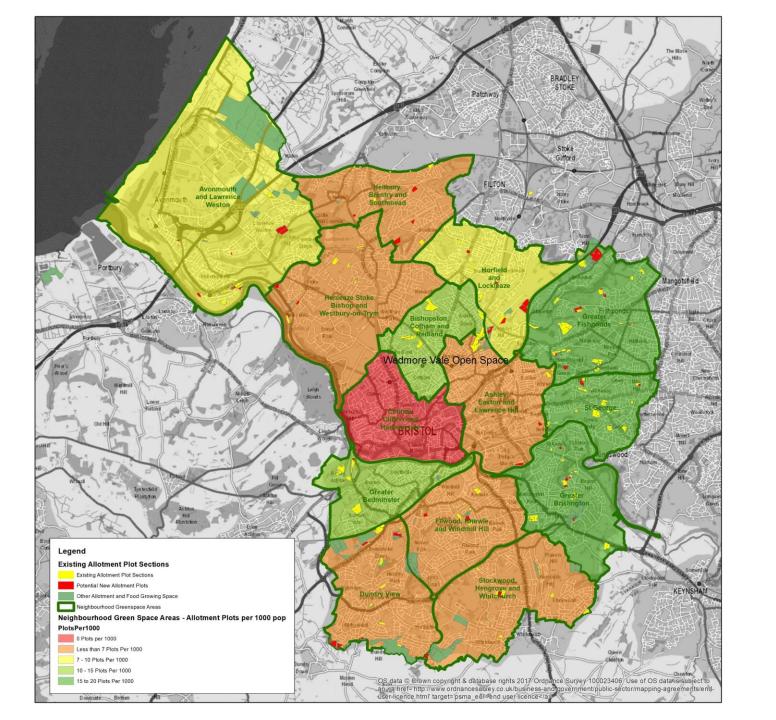

#### Tree and Woodland Strategy

Project work


Mapping

Engagement

ID	Task Name	Start	Finish	1 1	ember 2022 08 13 18 23	January 2023 28 02 07 12 17 22	February 202 27 01 06 11 16 2	3   March 2023 1   26   03   08   13   18   23	April 2023 3 28 02 07 12 17 2	May 2023 2 2 2 7 0 2 0 7 1 2 1 7 2	June 2023 22 27 01 06 11 16 2	July 2023 1 26 01 06 11 16 21	August 2023  26 31 05 10 15 20 2	September 2023   Oct 5 30 04 09 14 19 24 29 04
158	Tree and woodland strategy	Mon 19/12/2	Fri 01/09/23											¬
1	(One City) Bristol Tree Strategy	Mon 19/12/22	Fri 01/09/23											1
2	Engagement	Fri 10/02/23	Mon 03/04/23											
9	Project Work	Mon 19/12/22	Mon 01/05/23											
14	Document drafting	Sun 30/04/23	Fri 01/09/23											-
22	BCC Tree Strategy	Mon 19/12/22	Fri 01/09/23		0									1
23	Project work	Mon 19/12/22	Mon 01/05/23											
27	Document drafting	Mon 19/06/23	Fri 01/09/23											-

Land covered	One City Plan – all green space and streets BCC Plan – BCC owned and manged green space and streets
Time span	15 years
Outputs	City wide opportunity mapping (green spaces & streets) Councils approach to managing trees
Engagement	Public engagement Feb – March 2023 Forest of Nature (June)
Approval	One City Plan – Endorsed by One City Group (Sept onwards) BCC plan – (canopy linked to PGSS/M4N approved via PGSS), Street tree approval TBC

## Tree Canopy potential Sample Mapping DRAFT

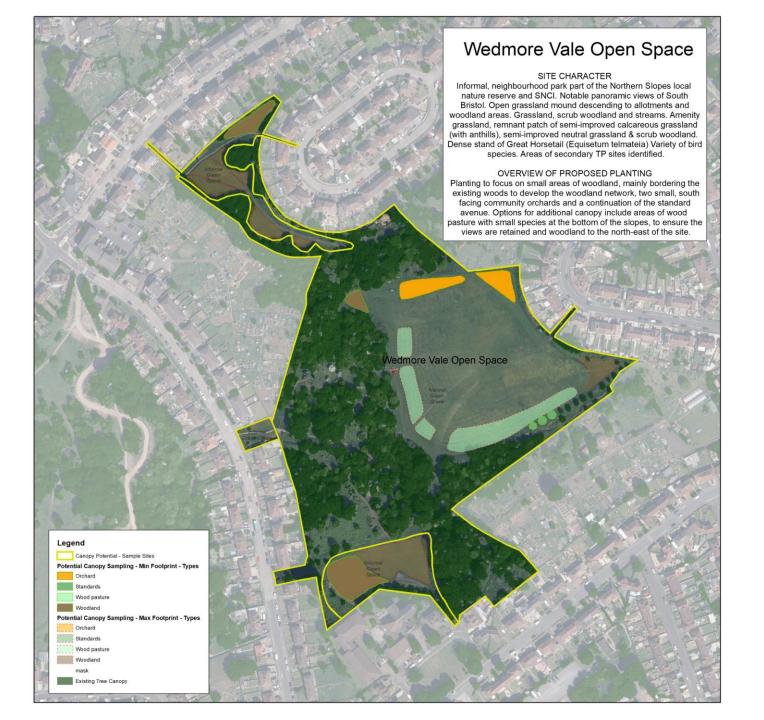


#### WoE Nature Recovery Network



Wetland

Grassland

Parks sites

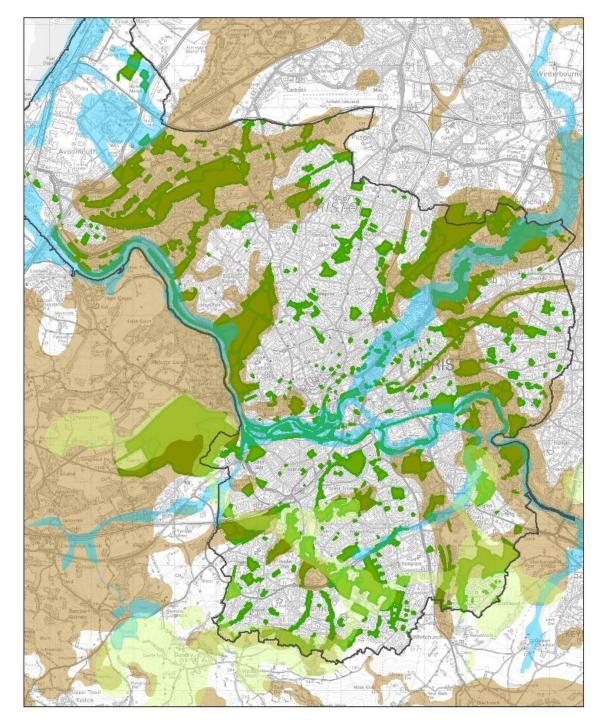

### Managing for Nature project


Project work


Mapping

Engagement

ID	Task Name	Start	Finish	Dr 28 0	December 2022   January 2023   February 2023   March 2023   April 2023   May 2023   June 2023   July 2023   August 2023   September 2023   O 28 03 08 13 18 23 28 02 07 12 17 22 27 01 06 11 16 21 26 01 06 11 0
159	Managing for Nature	Mon 05/12/2	Mon 27/03/2		
1	Managing for nature re-design	Mon 05/12/22	Mon 27/03/23		
2	Project work	Thu 12/01/23	Mon 13/03/23		
12	Mapping work	Mon 05/12/22	Mon 27/03/23		
18	Engagement work	Mon 13/02/23	Mon 20/03/23		

Land covered	All parks owned and managed land
Time span	Finished March 2023
Outputs	Evidence base and recommendations for how parks can manage more land for nature to contribute to city objectives, proposals for how we can better manage SNCIs
Engagement	Public engagement Feb – March 2023
Approval	As part of PGSS

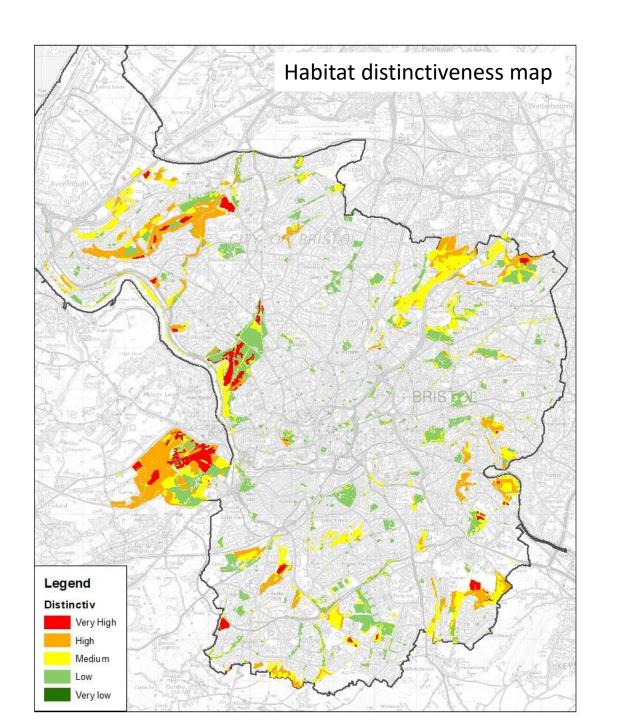

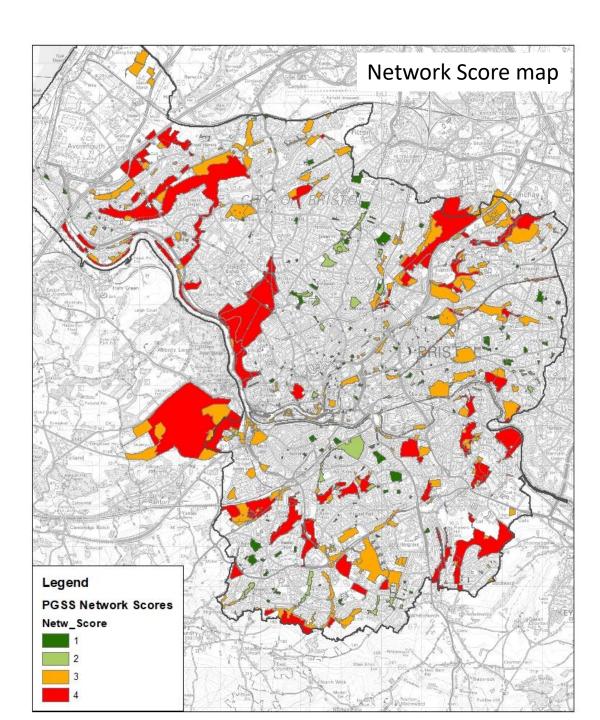

#### Parks and Green Spaces Strategy


Project work

Mapping

Engagement


ID	Task Name	Start	Finish		December 2022	February 2		May 2023	June 2023	July 2023	August 2023 26 31 05 10 15 20	September 2023   Octo 25 30 04 09 14 19 24 29 04
1	Parks and Green Spaces Stratgey	Wed 28/12/22	Tue 03/10/23	_	I							
2	Writing PGSS content	Wed 28/12/22	Thu 27/04/23		"							
19	Landuse mapping project	Fri 20/01/23	Fri 05/05/23									
51	Design and consultation	Mon 08/05/23	Mon 21/08/23	1								
59	PGSS Decision pathway (October Cabinet)	Mon 24/07/23	Tue 03/10/23									

Land covered	Parks owned green spaces, allotments, small holdings, crems and cems
Time span	15 years
Outputs	Protecting green space from development, How parks contribute to city objectives, Quality uplift, Land Use opportunity mapping
Engagement	Public consultation June - July 23
Approval	Cabinet Oct 23

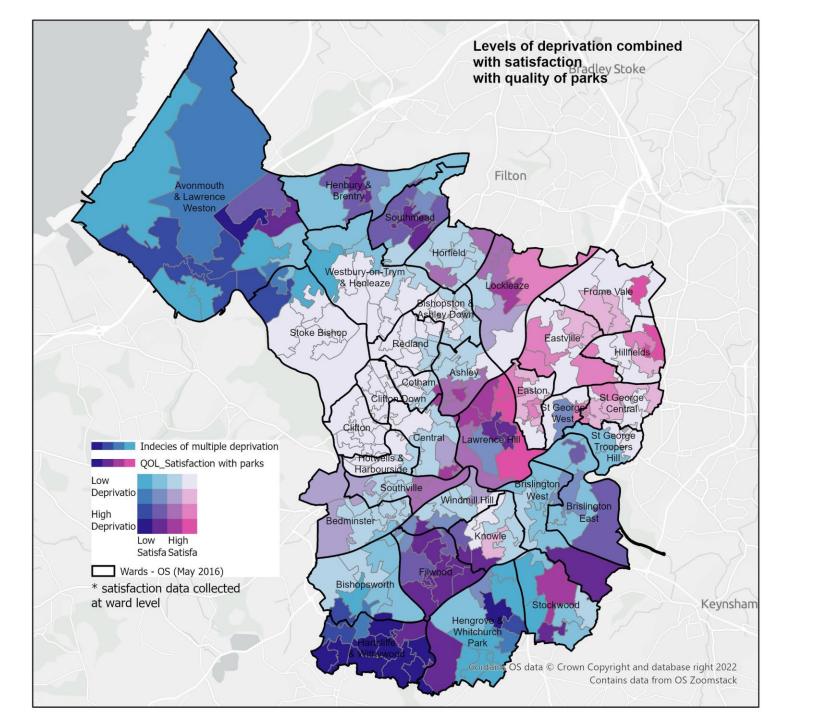


Quality of parks is lower in areas of deprivation


#### Formal Green Space Quantity provision

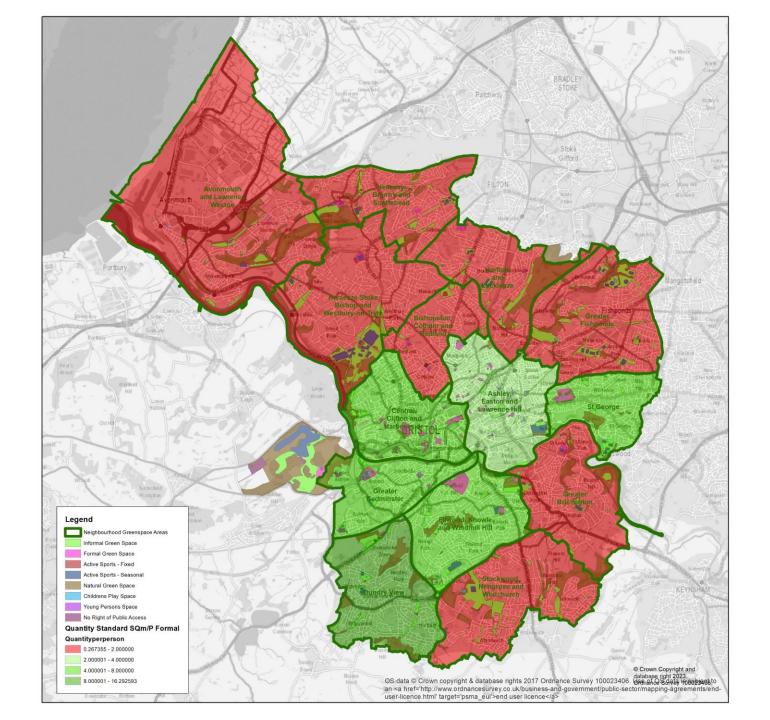


#### Informal Green Space Quantity provision

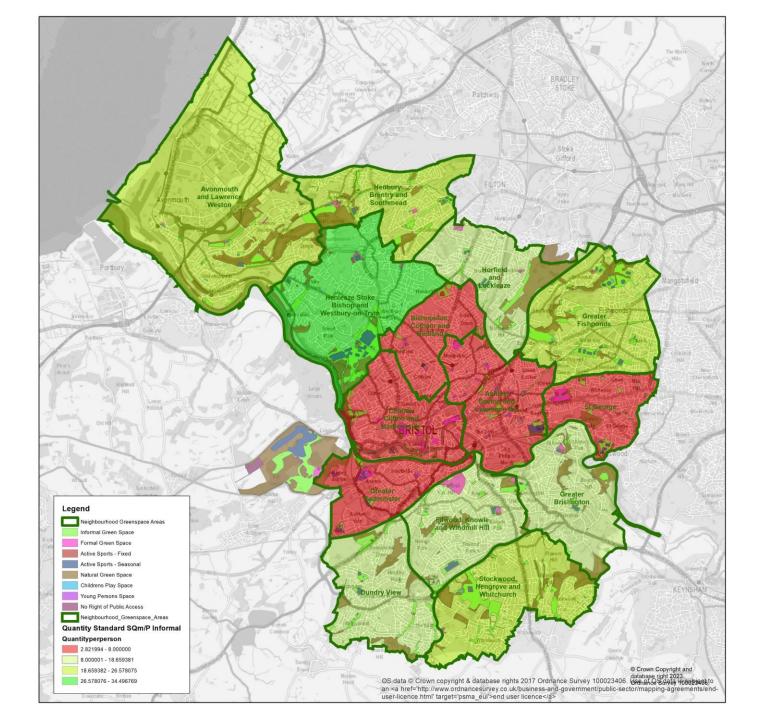


#### Natural Green Space Quantity provision

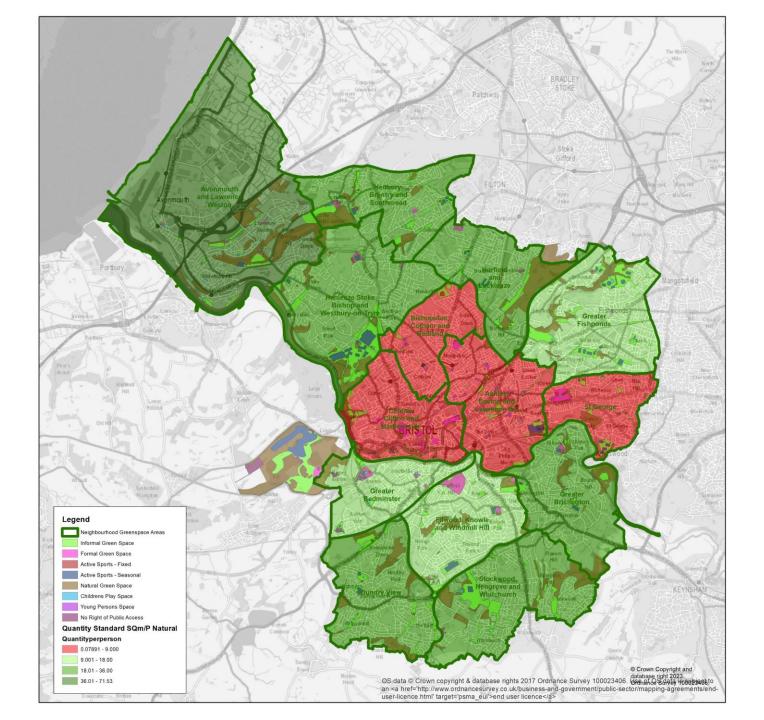

#### Play Space Quantity provision

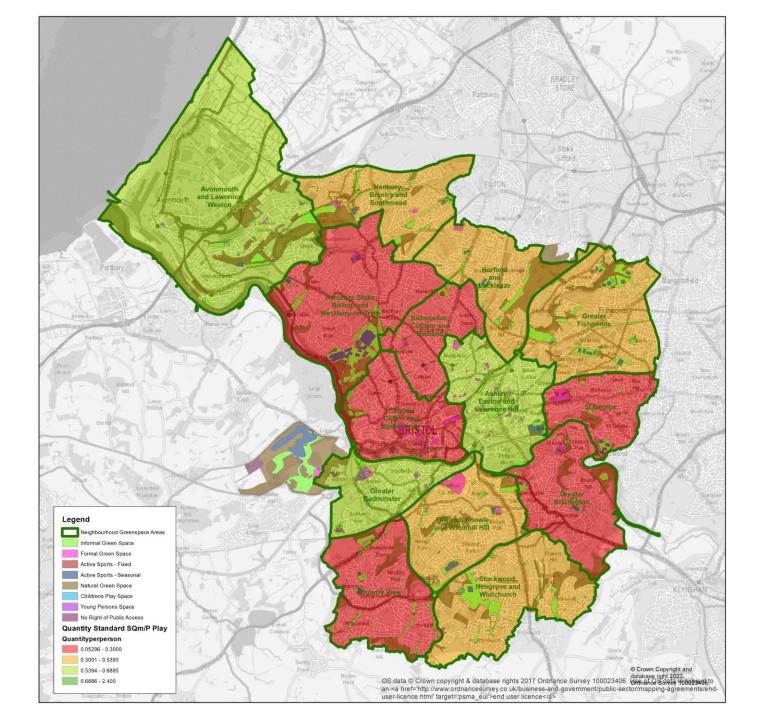

#### Overall Green Space Quantity provision

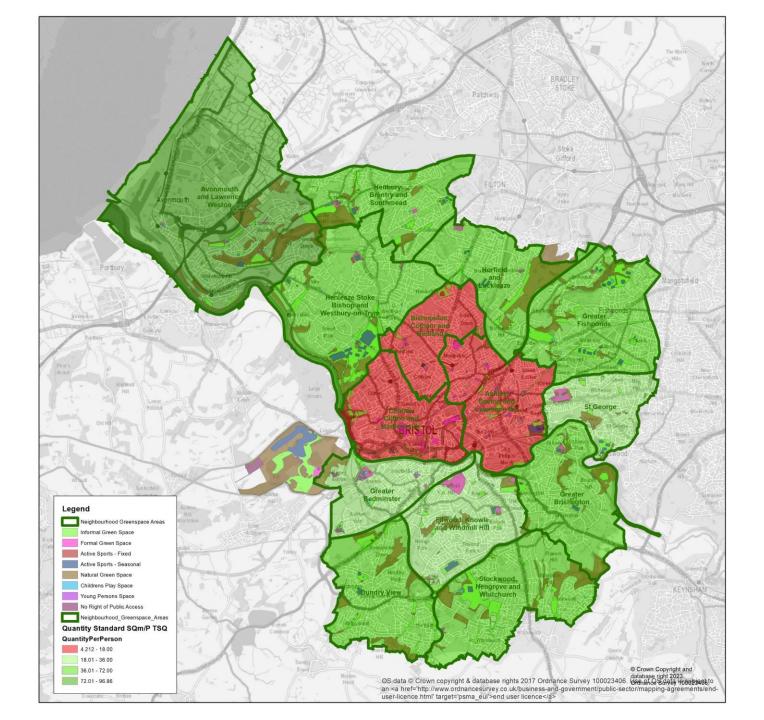

#### What will the PGSS tell us?

- Set a direction of travel and scale of ambition.
- It will create an evidence base that can be used to identify where there are opportunities to meet city needs.
- Define the priorities for each theme and where the areas of highest need & potential are.
- Headline actions and detail on what we hope to achieve in the first 5 years

#### What won't it tell us?

 It isn't an implementation plan – this will come afterwards.
